
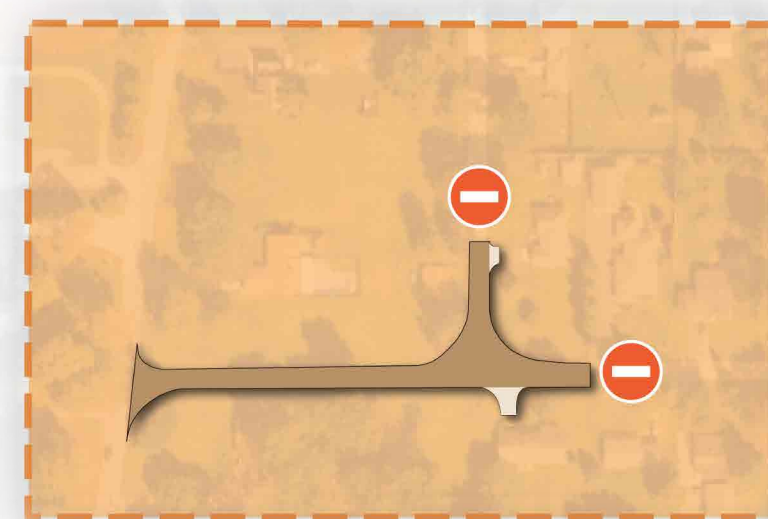


Construction Phasing

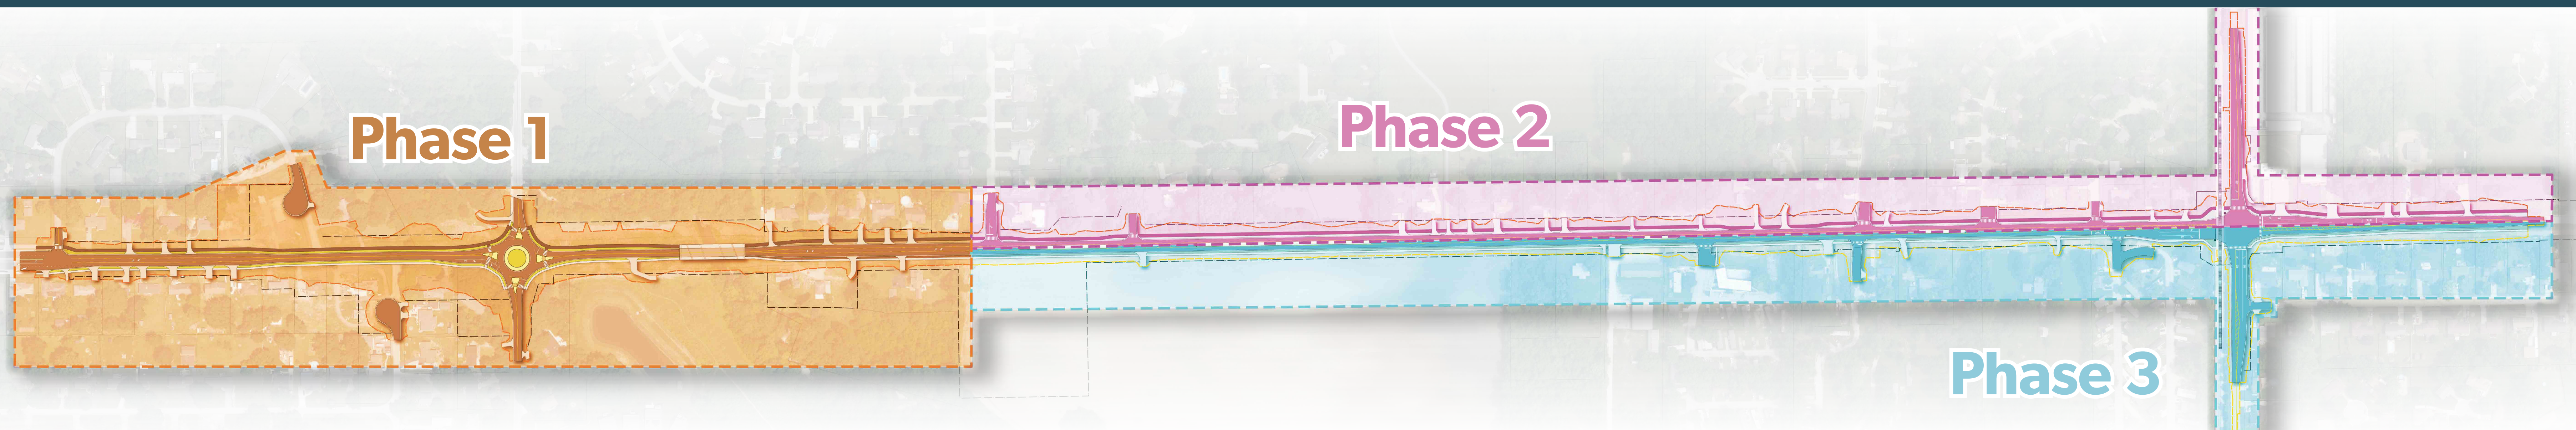

Mt. Pleasant S St.
Extension

Phase 1 (2028)

- Construction of the new alignment for Mt. Pleasant S. Street between Bluff Road and Mt. Pleasant W. Street.
- Full closure to through-traffic during construction.
- Full closure of County Line Road between Morris Road and Rocky Ridge Road.
- Construction of Pleasant Run Creek Bridge.
- Construction of Morgantown Road roundabout.

Phase 2 (2029)

- Closure of existing westbound travel lane while existing eastbound travel is maintained on County Line Road.
- Construction of proposed westbound lane on the north side of County Line Road.

Phase 3 (2029)

- Closure of existing westbound travel lane while existing eastbound travel is maintained on County Line Road.
- Construction of proposed eastbound lanes and median on the south side of County Line Road.

Construction Notes

- Detours will be provided to re-route traffic during closures.
- Access will be provided to all commercial and residential drives throughout construction, unless otherwise noted.
